
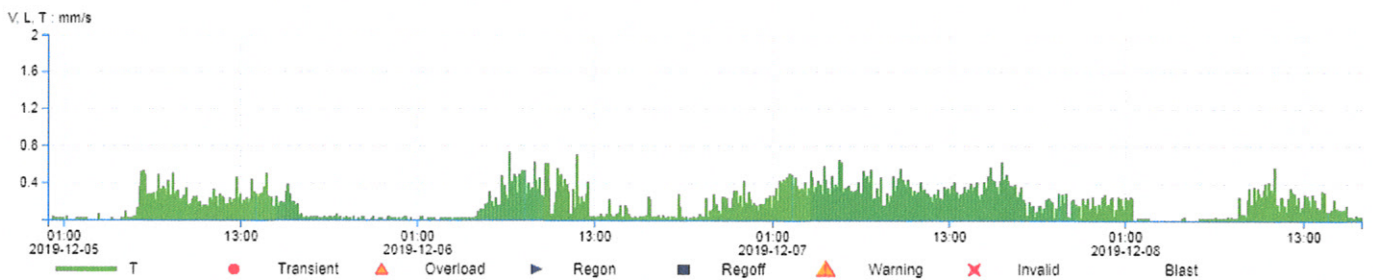
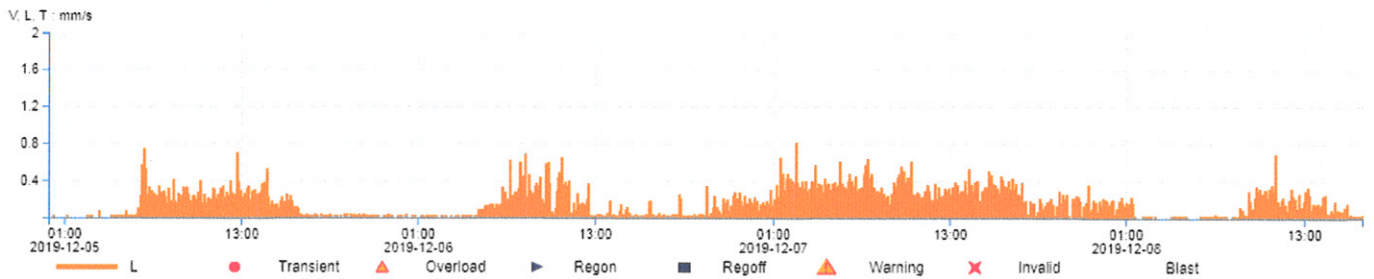


Project Bropakke 1a
Project maintainer -
Time frame 2019-12-05 00:00 - 2019-12-08 17:00 (Europe/Copenhagen)

14760, Kærgade 90, V12, S/N: 14760, Calibrated: 2019-01-13, (19) DIN4150-3 + Freq 25 mm/s 1-315Hz

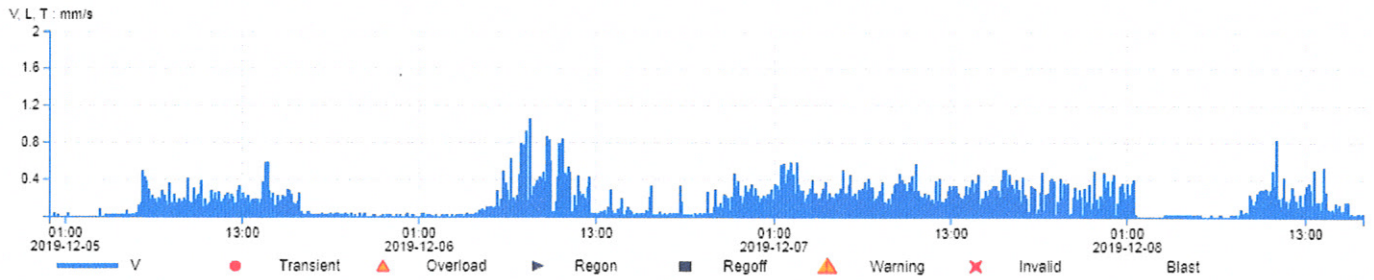

X-span 2019-12-05 00:00:00 - 2019-12-08 17:00:00
Y-span V, L, T : mm/s: 0.0 - 2.0

	V	L	T
Max	1.060 mm/s	0.81 mm/s	0.73 mm/s
Date	2019-12-06	2019-12-07	2019-12-06
Time	08:24:00	02:26:00	07:12:00
Hz	18	8	11
