
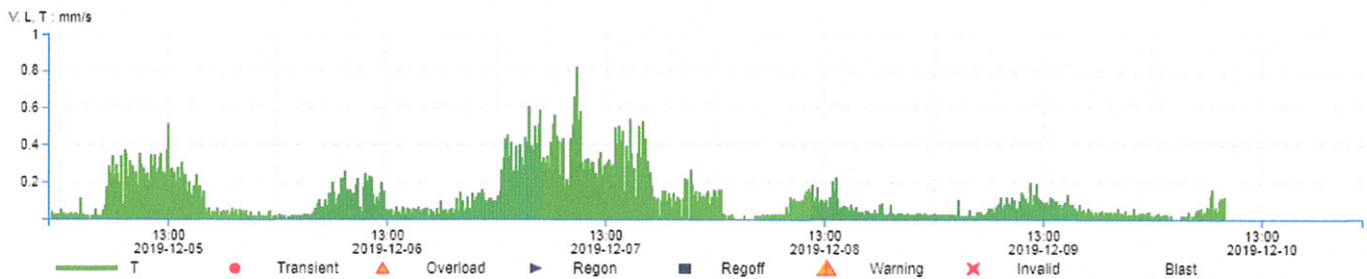
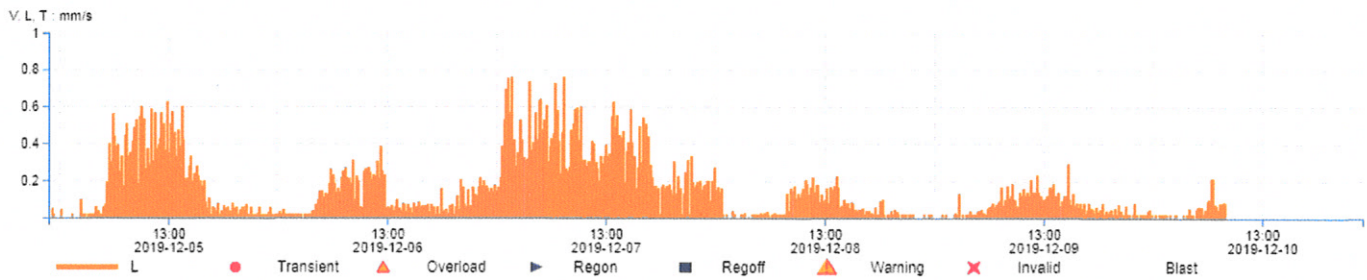


Project Bropakke 1a
Project maintainer -
Time frame 2019-12-05 00:00 - 2019-12-10 23:59 (Europe/Copenhagen)

4690, Kærgade 98E, V12, S/N: 4690, Calibrated: 2018-02-07, (19) DIN4150-3 + Freq 25 mm/s 1-315Hz

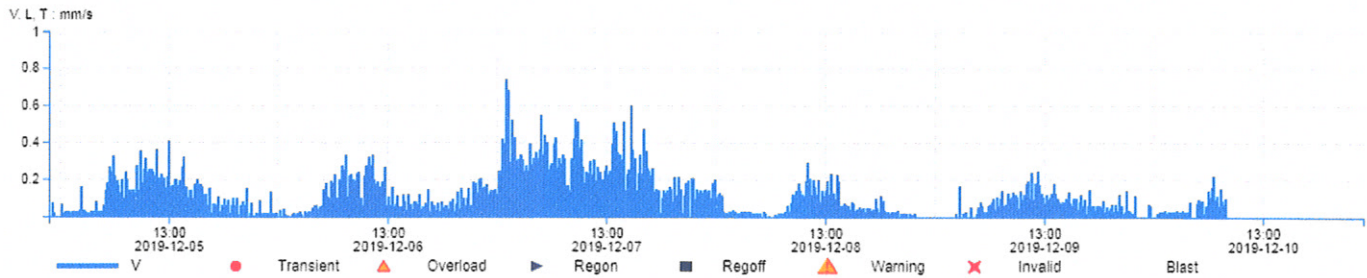

X-span 2019-12-05 00:00:00 - 2019-12-10 23:59:00

Y-span V, L, T : mm/s: 0.0 - 1.0

	V	L	T
Max	0.74 mm/s	0.76 mm/s	0.82 mm/s
Date	2019-12-07	2019-12-07	2019-12-07
Time	01:54:00	02:26:00	09:40:00
Hz	12	7.5	10
